



Community Newsletter

Construction update  
June/July 2022

# Consort Place



CGI view of East Tower and Manilla Street public space.

## Local people to help build Consort Place

We are working with Tower Hamlets Council to help provide jobs and apprenticeships to local people.

### Would you like to help build Consort Place?

Please express an interest at:

[consortplaceconstruction@secnewgate.co.uk](mailto:consortplaceconstruction@secnewgate.co.uk)

## Keeping in touch

We produce monthly newsletters updating the local community on progress at Consort Place.

**We can also text and email you our latest news – please contact us to register.**

07718 489739 | [consortplaceconstruction@secnewgate.co.uk](mailto:consortplaceconstruction@secnewgate.co.uk) | [www.consortplaceconstruction.com](http://www.consortplaceconstruction.com)

## Thames Water works

As residents will hopefully be aware, in mid June 2022 Thames Water began works to upgrade a water main running underneath Byng Street. The work is not related to the Consort Place project but we are working closely with Thames Water to ensure that their works and our construction activity cause the minimum disruption to residents.

Thames Water's works will progress in stages along with the length of Byng Street. The work is due to be completed in October 2022.



Recent photo showing progress at the West Tower.



## Our construction update

### June construction update

#### West Tower

- Concrete placement boom will continue to pour concrete for the frame.
- Façade installation continued.
- Apartment fit out (including kitchens) continued on lower floors.

#### East Tower and Hotel Tower

- Concrete pouring from the slipform rig to build the tower's core and frame.
- Façade installation continued.
- Apartment fit out continued on lower floors.

### Our plan for July

#### West Tower

- Concrete frame will complete.
- Façade installation will continue.
- Apartment fit-out (second fix and decoration) continues.

#### East Tower and Hotel Tower


- Slipform will continue to pour concrete for the towers' core and frame.
- Façade installation will continue.
- Apartment fit-out continues.
- TC2 Crane will rise in height again.
- Hotel (Byng Street) Slipform Rig dismantling will complete.
- Installation of new hoist lifts continues.

## Our working hours

Our standard working hours are:

**Monday to Friday 8am-6pm and Saturday 8am-1pm**

We apologise for any inconvenience caused and thank residents for their patience.

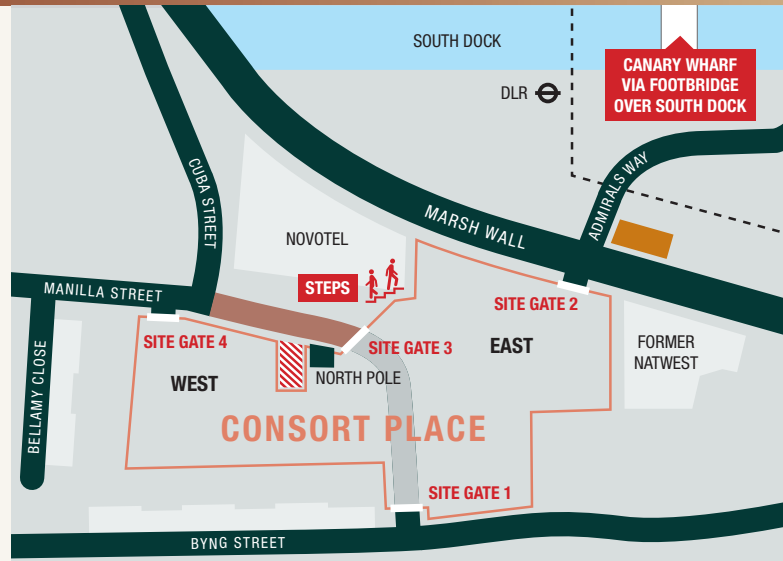

Recent site photo showing activity on Manilla Street.

### Consort Place: Who's Who?



**FEC**  
Developer



**Midgard**  
Principal Contractor



**SEC Newgate**  
Engaging with the local community

## Keeping in touch

We produce monthly newsletters updating the local community on progress at Consort Place.

**We can also text and email you our latest news – please contact us to register.**

07718 489739 | consortplaceconstruction@secnewgate.co.uk | www.consortplaceconstruction.com
