



Community Newsletter

Construction update  
March/April 2023

# Consort Place

## Consort Place community newsletter

Our newsletters keep the community up to date with construction at Consort Place



An evening rendering of the new Aspen Square looking opposite from the East Tower

## Both towers climb high with continued façade installation

In March we began school lift works and façade installation on the West Tower, while we continued with façade installation and apartment fit-outs on the East Tower. In April we expect to complete façade installation at the roof level on the West Tower while continuing with façade and framework installation on the Hotel Tower.

## Local people to help build Consort Place

We are working with Tower Hamlets Council to help provide jobs and apprenticeships to local people.

### Would you like to help build Consort Place?

Please express an interest at: [consortplaceconstruction@secnewgate.co.uk](mailto:consortplaceconstruction@secnewgate.co.uk)

## Keeping in touch

We produce monthly newsletters updating the local community on progress at Consort Place.

We can also text and email you our latest news – please contact us to register.

07778 665906 | [consortplaceconstruction@secnewgate.co.uk](mailto:consortplaceconstruction@secnewgate.co.uk) | [www.consortplaceconstruction.com](http://www.consortplaceconstruction.com)



Recent photo showing façade installation to both towers





## Our construction update

### March construction update | West Tower

- Continued façade installation to roof level
- Ongoing second fix and decoration of apartments
- M+E roof plant continued
- Hoist removal continued
- School lift works and façade began

### East Tower and Hotel Tower

- Continued concrete pouring for the East Tower's core and frame
- Works on the hotel frame and façade continued
- Façade installation continued
- Apartment fit-out continued
- Crane lift increased in height

### Our plan for April | West Tower

- Façade installation will complete at roof level
- Ongoing apartment fit-out
- Continued M+E roof planting
- Installing the school hoist
- Continued works on the school lift and façade
- Expected switchover to permanent power

### East Tower and Hotel Tower

- Continued pouring of concrete for the East Tower's core and frame
- Ongoing works to hotel frame and façade installation
- Apartment fit-out will continue
- Crane lift will increase in height

## Our working hours

Our standard working hours are:

**Monday to Friday 8am-6pm and Saturday 8am-1pm**

We apologise for any inconvenience caused and thank residents for their patience.

## Consort Place: Who's Who?




FEC Developer



Midgard Principal Contractor



SEC Newgate Engaging with the local community

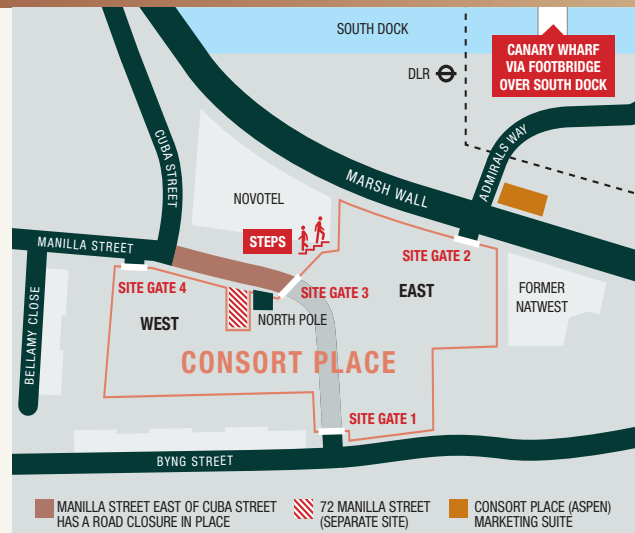

Recent ground-level photo from Marsh Wall showing construction progress on the East Tower



## Keeping in touch

We produce monthly newsletters updating the local community on progress at Consort Place.

We can also text and email you our latest news – please contact us to register.

07778 665906 | consortplaceconstruction@secnewgate.co.uk | www.consortplaceconstruction.com
